

PES1UG24AM462
GREESHMA G
AIML SEC-H
Lab 2: Agile Backlog Creation & Sprint Simulation in Jira


PROBLEM STATEMENT #37
Group Travel Expense Simplification Engine


SCREENSHOT 1:

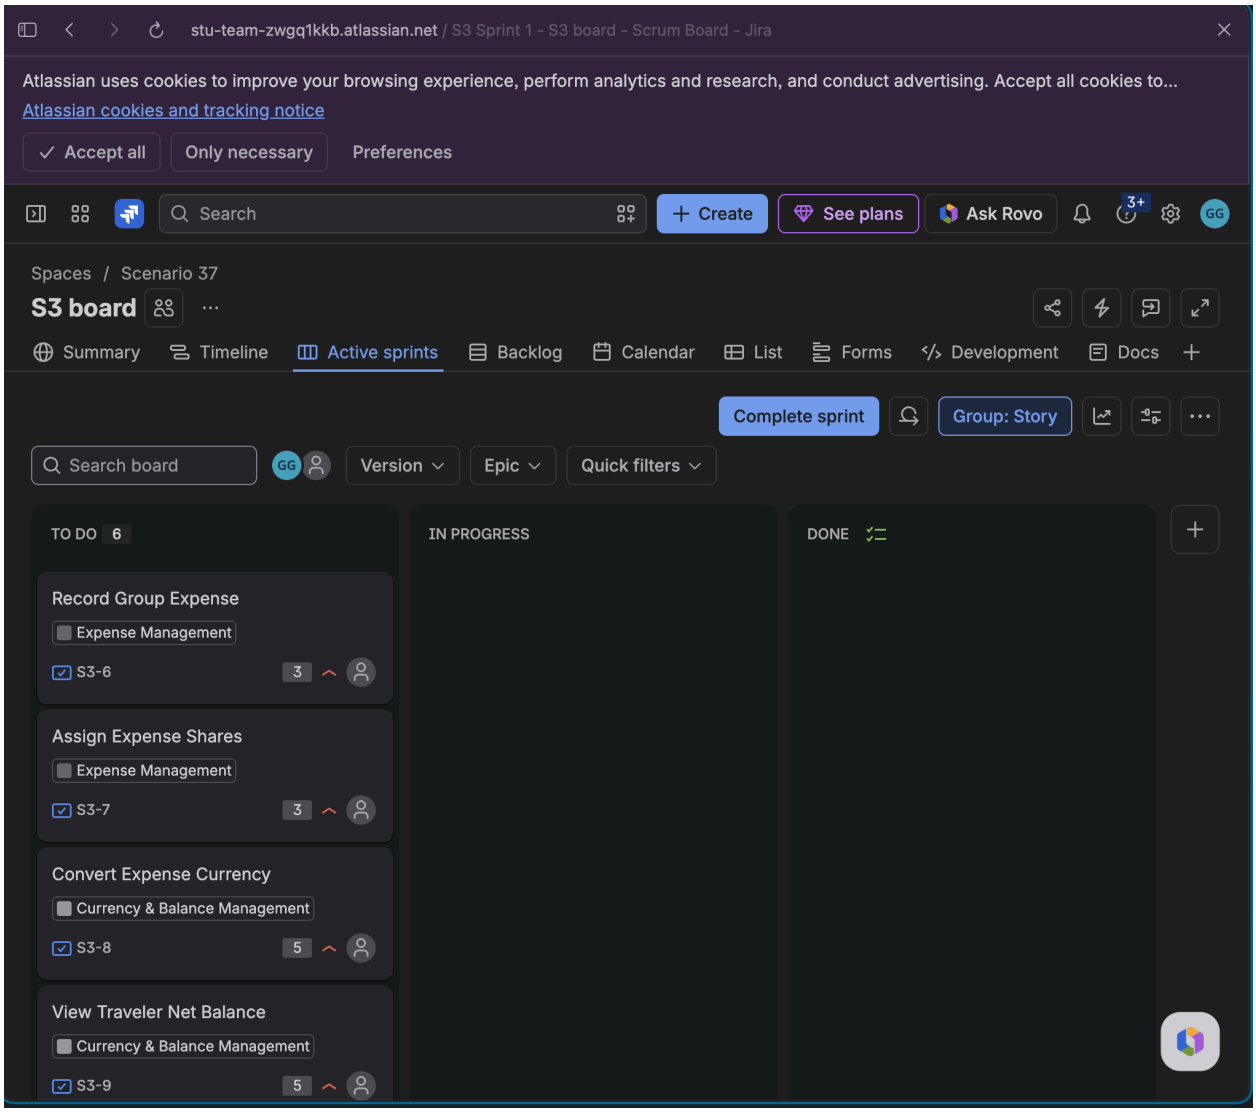


SCREENSHOT 2:

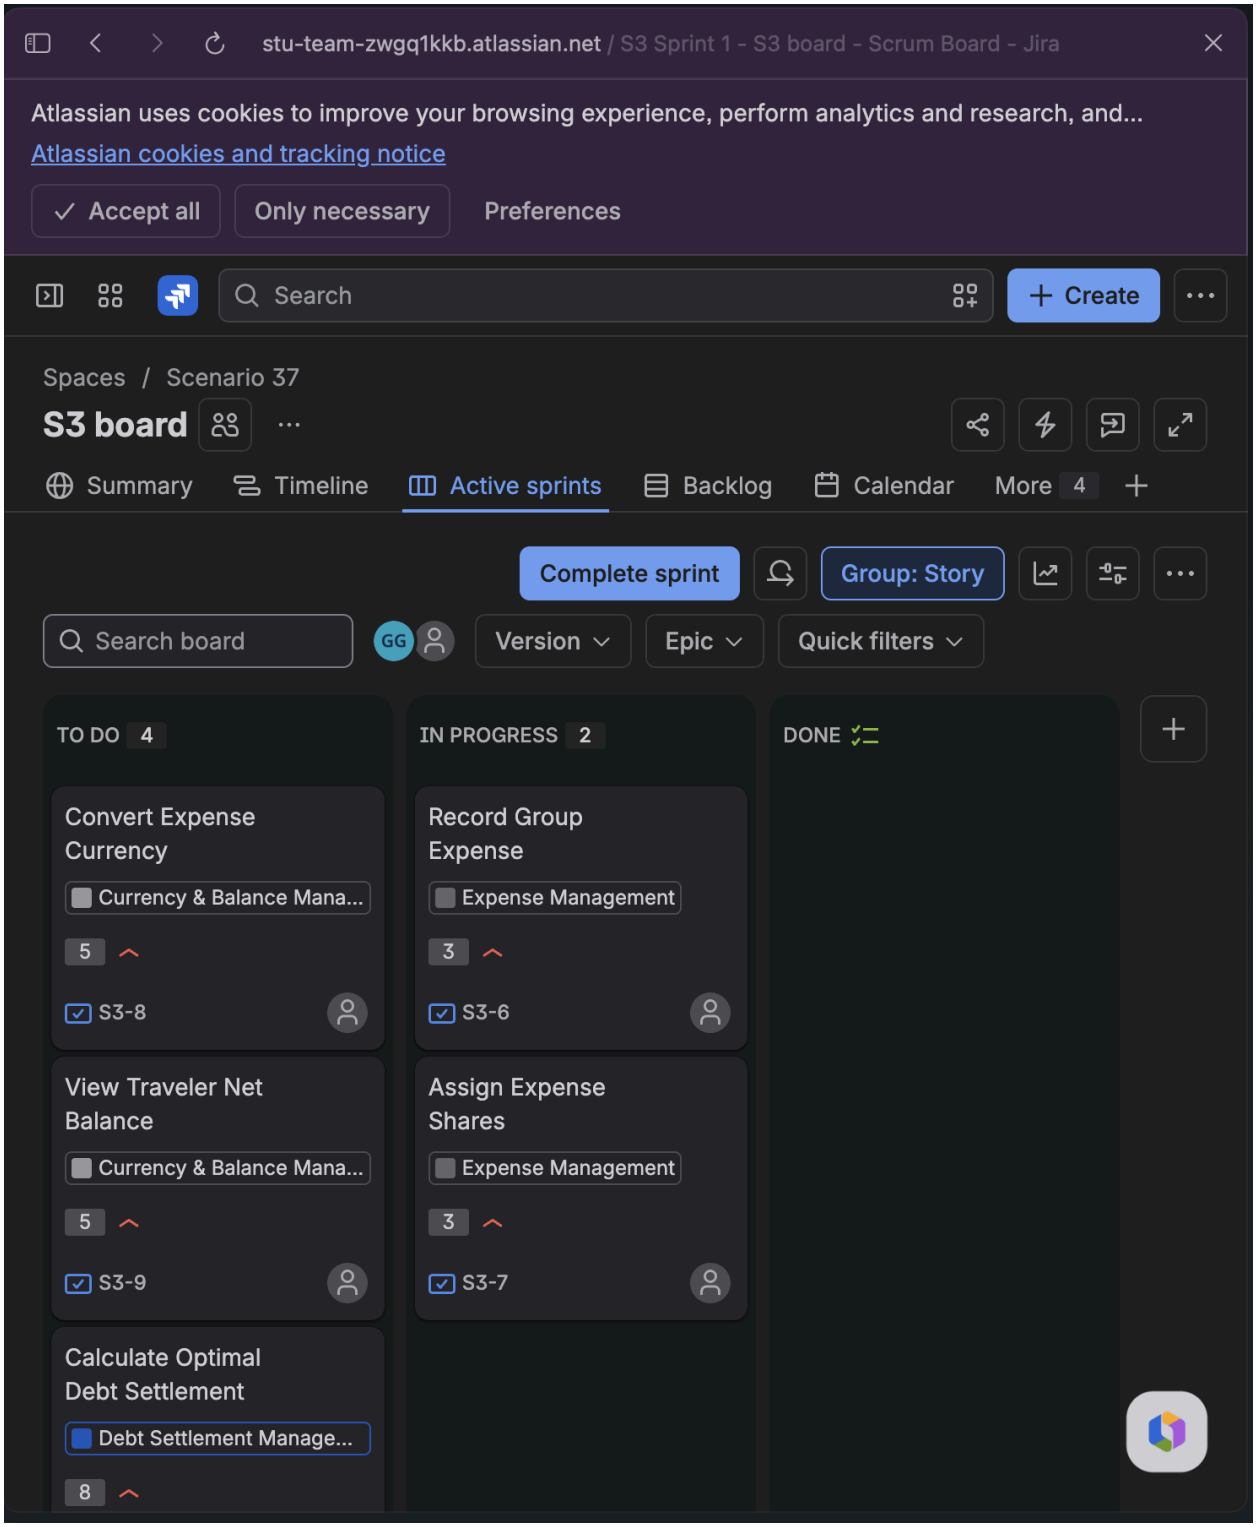


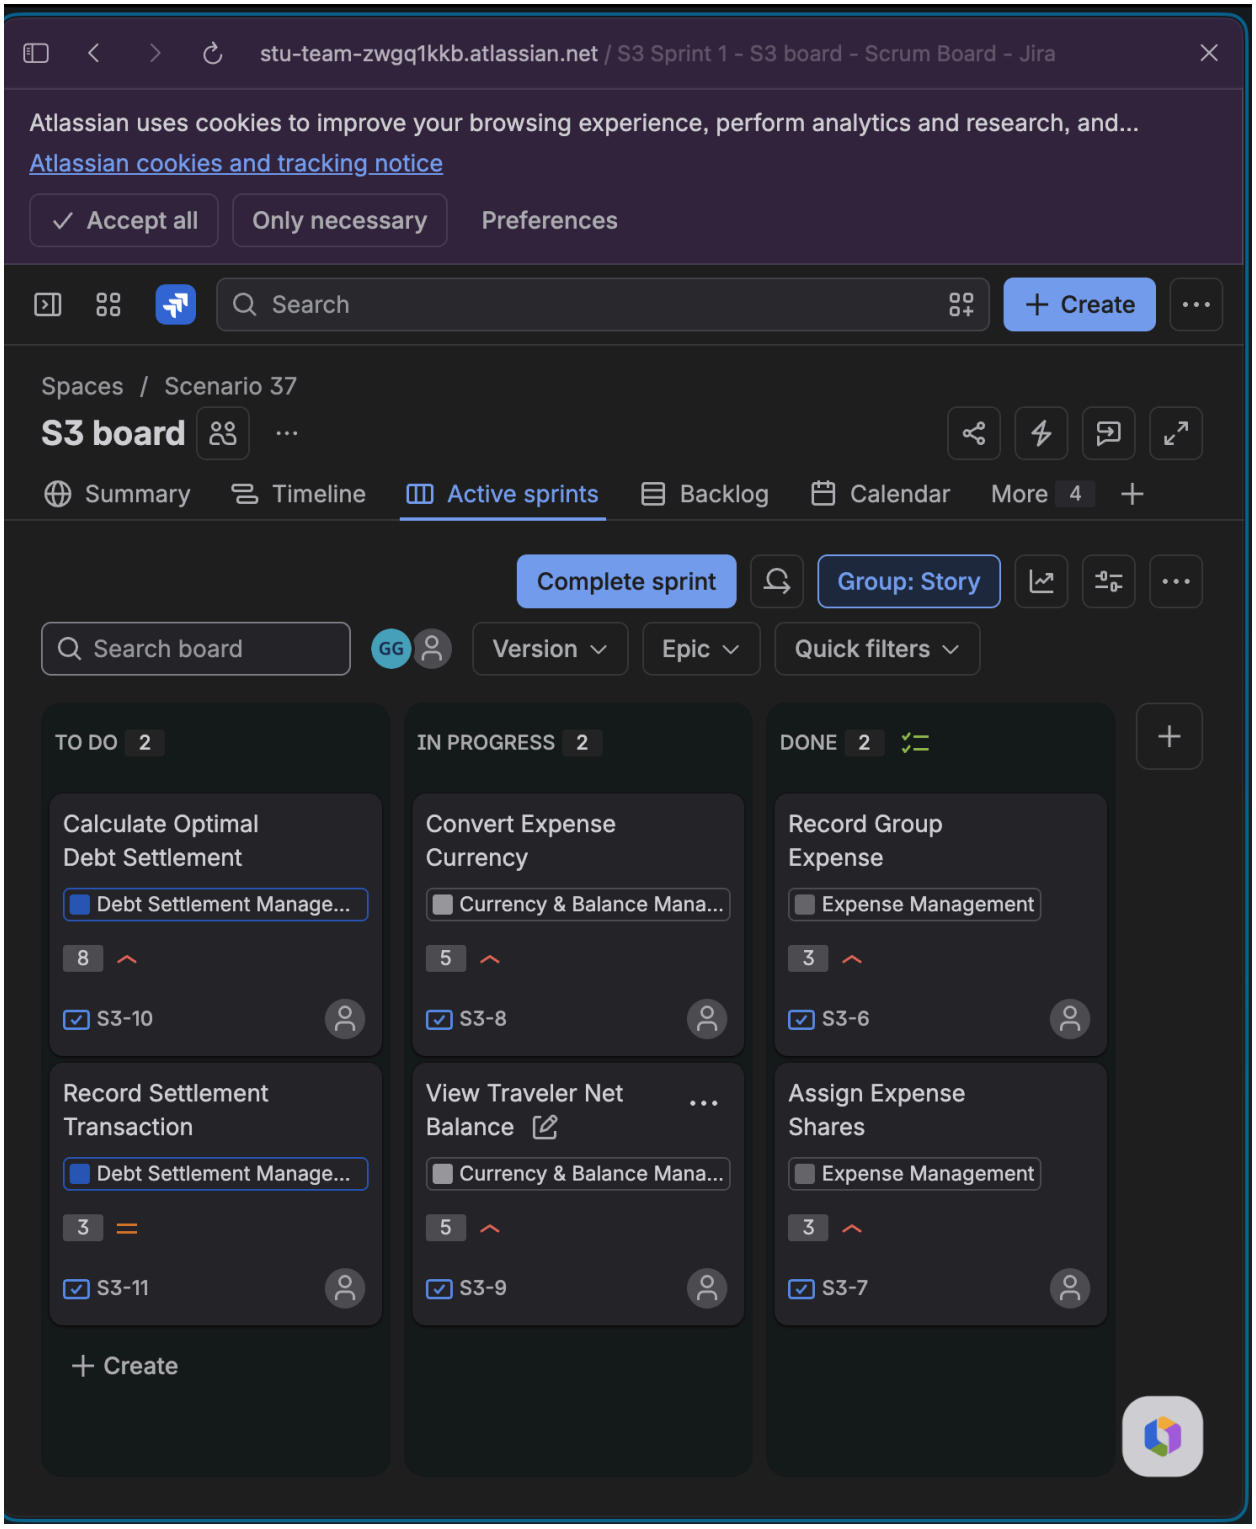

stu-team-zwgq1kkb.atlassian.net / S3 Sprint 1 - S3 board - Scrum Board - Jira
Atlassian uses cookies to improve your browsing experience, perform analytics and research, and...
Atlassian cookies and tracking notice
Accept all
Only necessary
Preferences
Search
Create
Spaces / Scenario 37
S3 board
Summary
Timeline
Active sprints
Backlog
Calendar
More 4
Complete sprint
Group: Story
Search board
GG
Version
Epic
Quick filters
TO DO 2
IN PROGRESS 2
DONE 2
Calculate Optimal Debt Settlement
Debt Settlement Manage...
8
S3-10
Convert Expense Currency
Currency & Balance Mana...
5
S3-8
Record Group Expense
Expense Management
3
S3-6
Record Settlement Transaction
Debt Settlement Manage...
3
S3-11
View Traveler Net Balance
Currency & Balance Mana...
5
S3-9
Assign Expense Shares
Expense Management
3
S3-7
Create

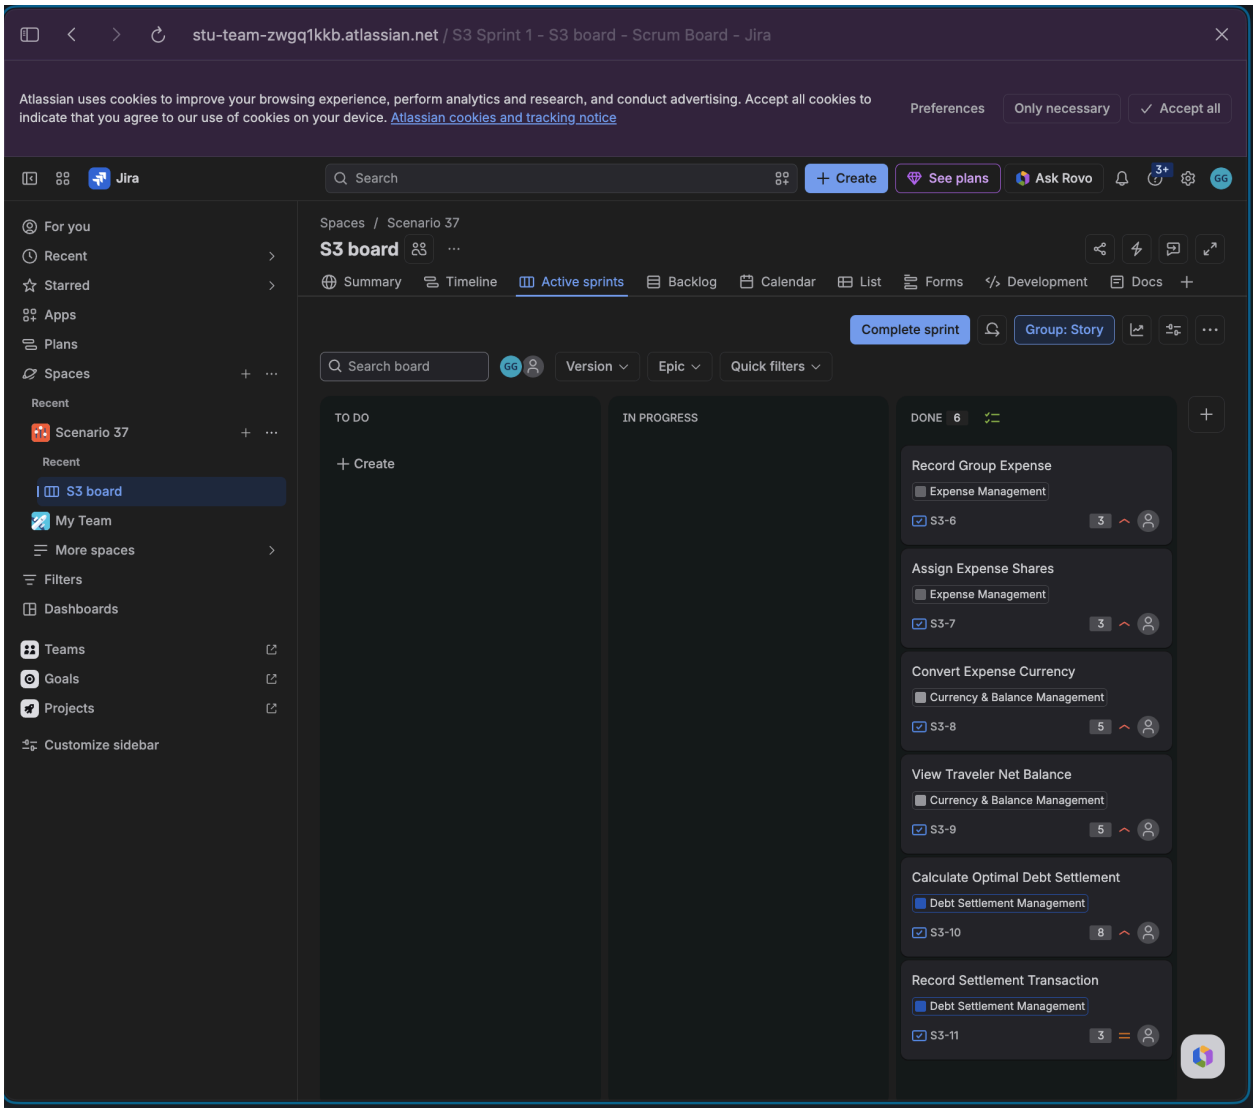



SCREENSHOT 3:

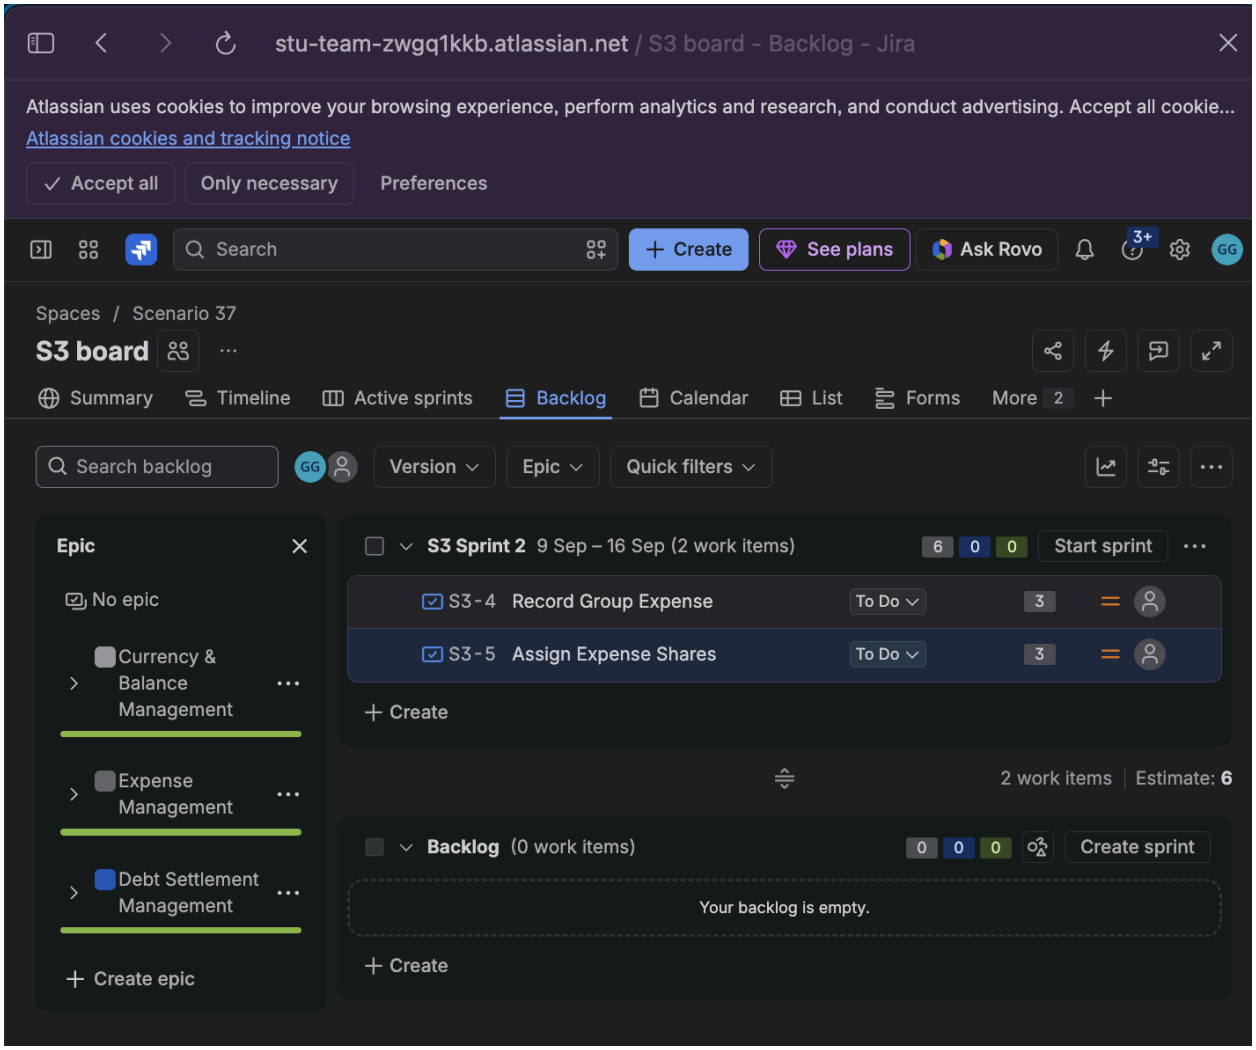
stu-team-zwgq1kkb.atlassian.net / S3 board - Backlog - Jira
Atlassian uses cookies to improve your browsing experience, perform analytics and research, and conduct advertising. Accept all cookie...
Atlassian cookies and tracking notice
Accept all
Only necessary
Preferences
Search
Create
See plans
Ask Rovo
3+
GG
Spaces / Scenario 37
S3 board
Summary
Timeline
Active sprints
Backlog
Calendar
List
Forms
More 2
Search backlog
Version
Epic
Quick filters
Epic
No epic
Currency & Balance Management
Expense Management
Debt Settlement Management
Create epic
S3 Sprint 2 9 Sep – 16 Sep (2 work items)
6 0 0
Start sprint
S3-4 Record Group Expense
To Do
3
S3-5 Assign Expense Shares
To Do
3
Create
2 work items | Estimate: 6
Backlog (0 work items)
0 0 0
Create sprint
Your backlog is empty.
Create

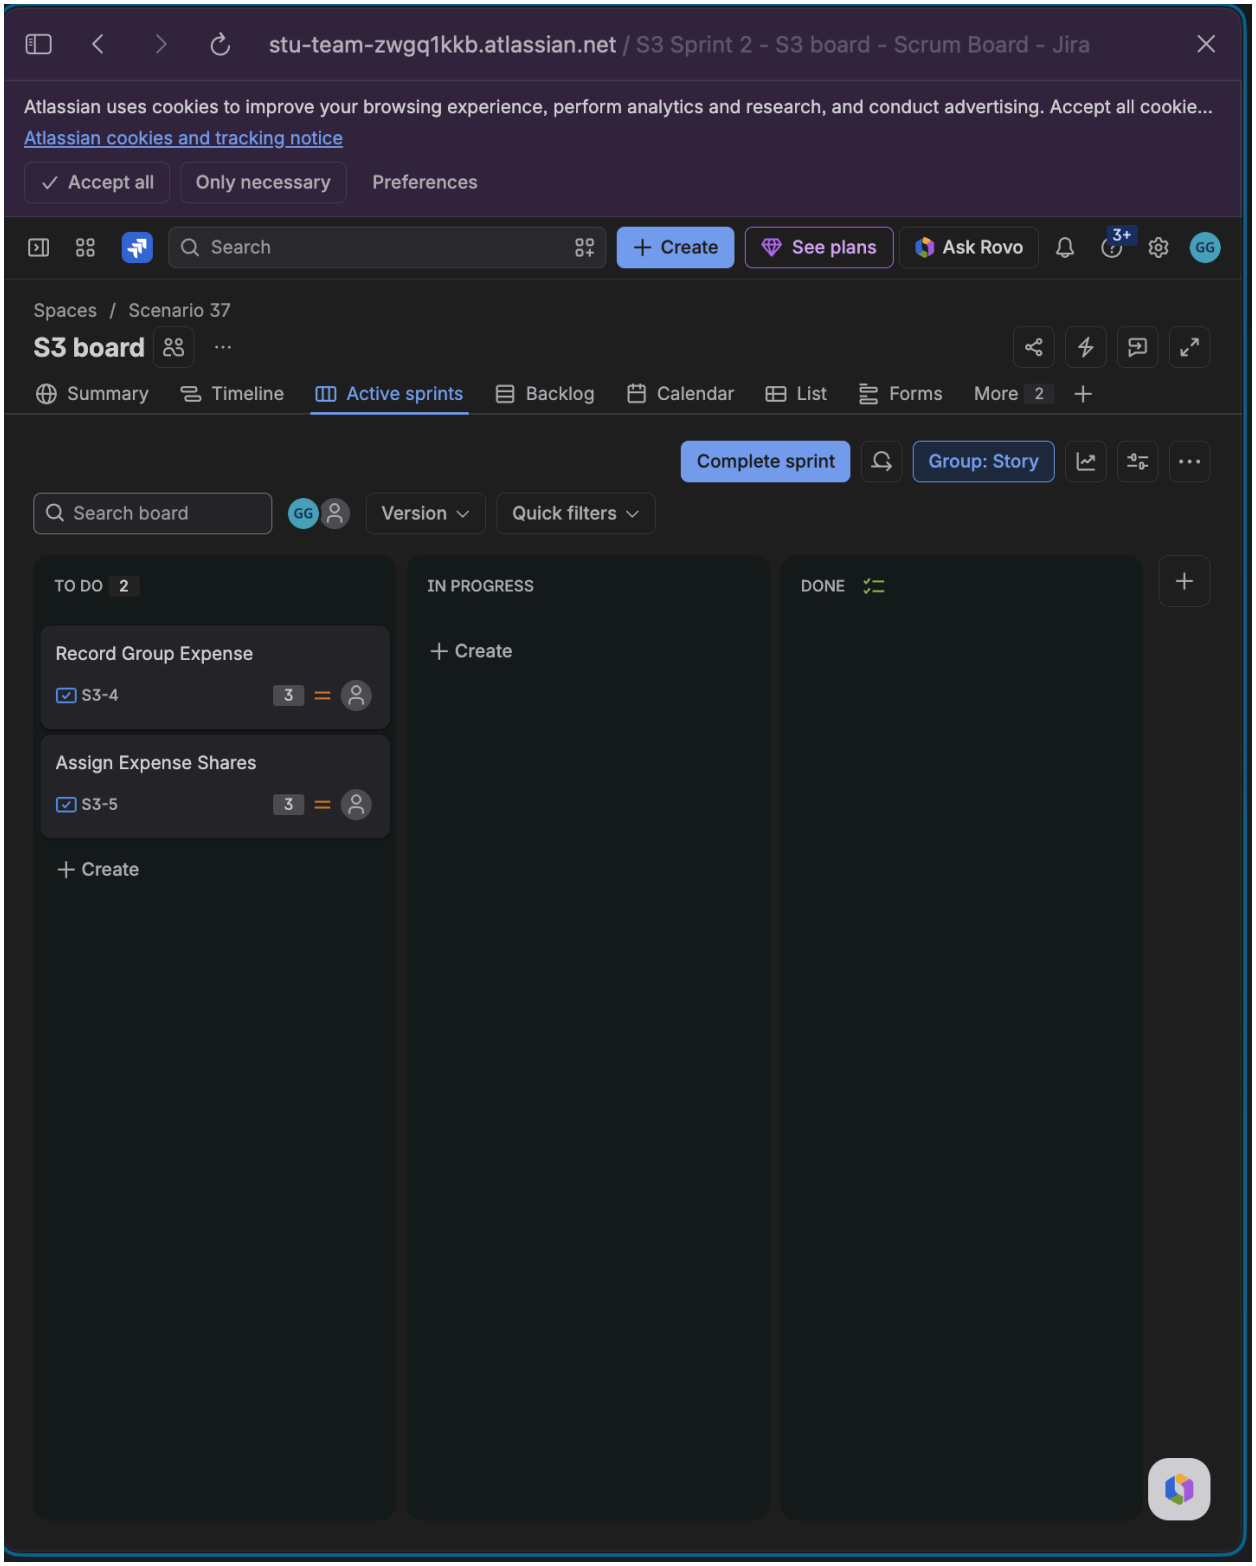

stu-team-zwgq1kkb.atlassian.net / S3 Sprint 2 - S3 board - Scrum Board - Jira
Atlassian uses cookies to improve your browsing experience, perform analytics and research, and conduct advertising. Accept all cookie...
Atlassian cookies and tracking notice
Accept all
Only necessary
Preferences
Search
Create
See plans
Ask Rovo
3+
GG
Spaces / Scenario 37
S3 board
Summary
Timeline
Active sprints
Backlog
Calendar
List
Forms
More 2
Complete sprint
Group: Story
Search board
Version
Quick filters
TO DO 2
IN PROGRESS
DONE
Record Group Expense
S3-4
3
Assign Expense Shares
S3-5
3
Create
Create

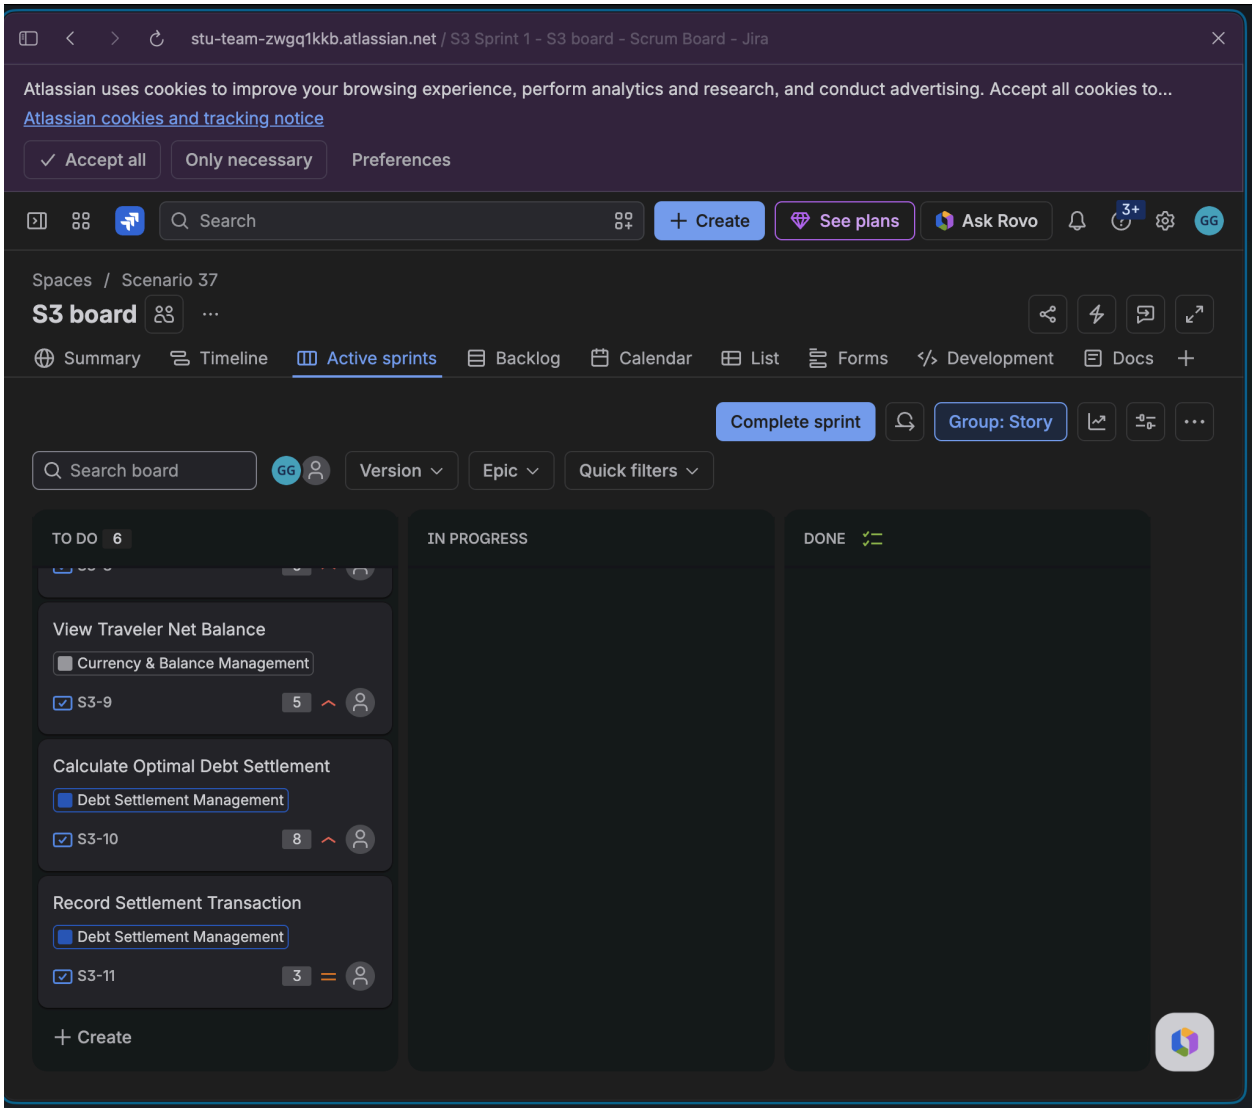
stu-team-zwgq1kkb.atlassian.net / S3 Sprint 1 - S3 board - Scrum Board - Jira
Atlassian uses cookies to improve your browsing experience, perform analytics and research, and conduct advertising. Accept all cookies to...
Atlassian cookies and tracking notice
Accept all
Only necessary
Preferences
Search
Create
See plans
Ask Rovo
3+
GG
Spaces / Scenario 37
S3 board
Summary
Timeline
Active sprints
Backlog
Calendar
List
Forms
Development
Docs
Complete sprint
Group: Story
Search board
Version
Epic
Quick filters
TO DO 6
IN PROGRESS
DONE
View Traveler Net Balance
Currency & Balance Management
S3-9
5
Calculate Optimal Debt Settlement
Debt Settlement Management
S3-10
8
Record Settlement Transaction
Debt Settlement Management
S3-11
3
Create

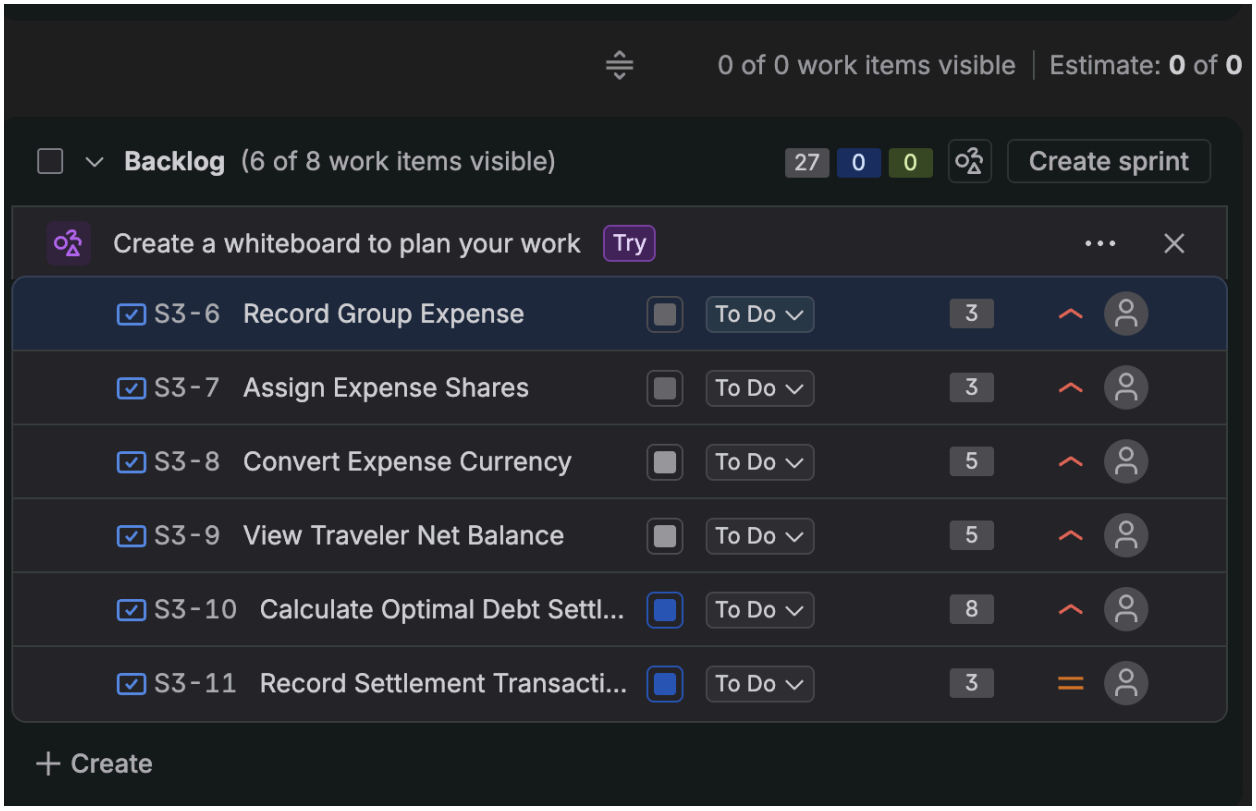
0 of 0 work items visible
Estimate: 0 of 0
Backlog (6 of 8 work items visible)
27
0
0
Create sprint
Create a whiteboard to plan your work
Try
S3-6 Record Group Expense
To Do
3
S3-7 Assign Expense Shares
To Do
3
S3-8 Convert Expense Currency
To Do
5
S3-9 View Traveler Net Balance
To Do
5
S3-10 Calculate Optimal Debt Settl...
To Do
8
S3-11 Record Settlement Transacti...
To Do
3
Create

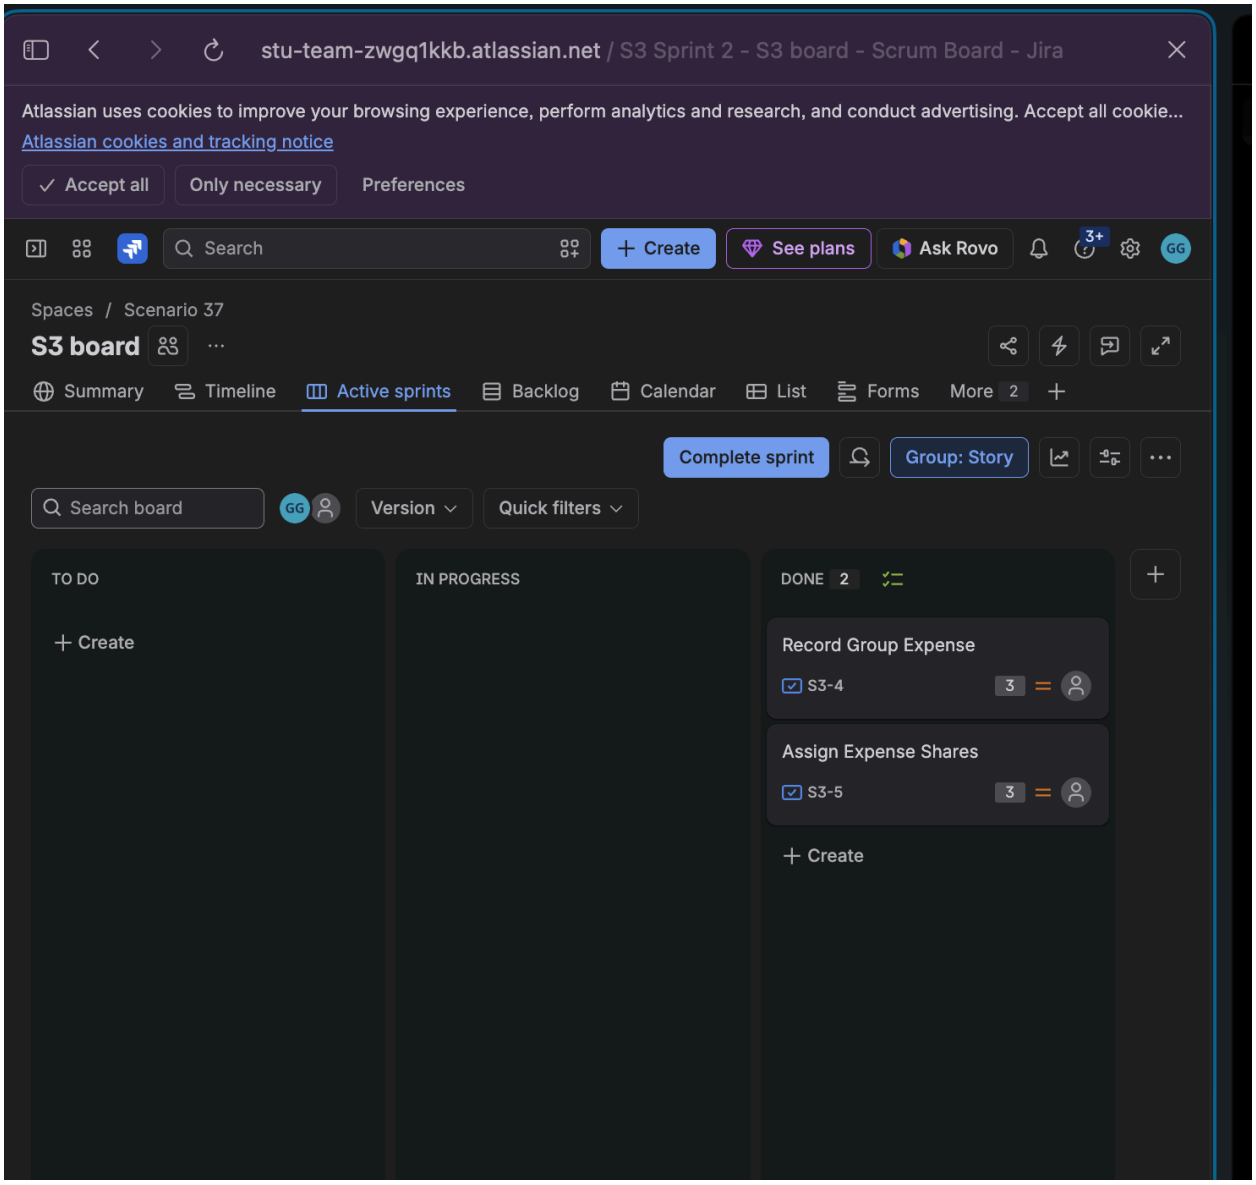

SCREENSHOT 4:

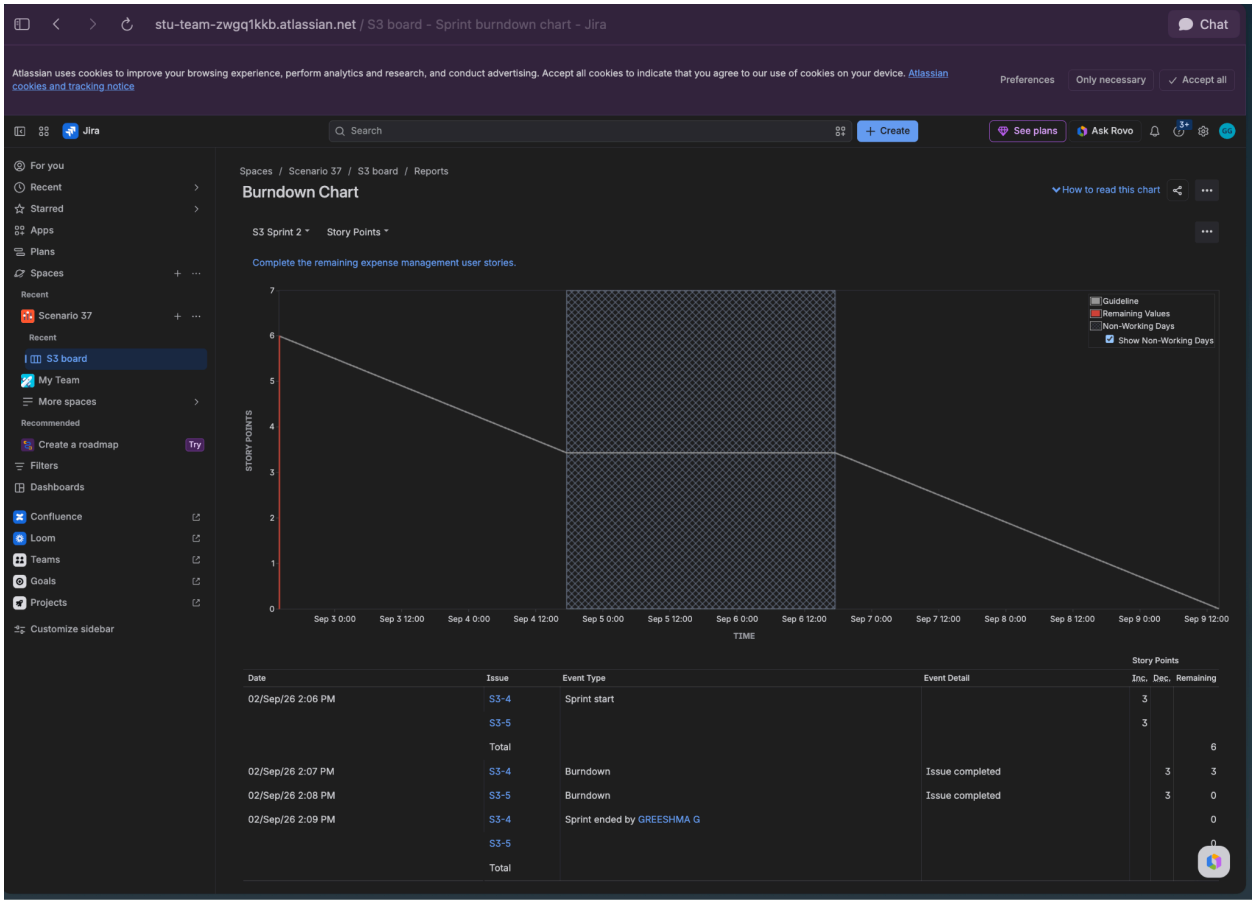

Reflection

1. Did your estimations reflect the actual effort?

Yes, the story point estimations reasonably reflected the effort required for the selected user stories. The stories were estimated using the Fibonacci sequence, which was used to represent effort, complexity, and uncertainty. In Sprint 2, “Record Group Expense” and “Assign Expense Shares” were each assigned 3 story points, giving a total of 6 story points. Both user stories were completed during the simulated sprint, indicating that the estimates were appropriate for the planned work.

2. Was your backlog well-prioritized?

Yes, the backlog was prioritized according to the importance of the functionality and the needs of the end user. The user stories were arranged in an order that allowed important expense-management functionality to be selected for the sprint. This helped ensure that the most relevant work was addressed first and that the sprint had a clear focus.

3. How did your simulated sprint align with your plan?

The simulated sprint aligned well with the planned work. The selected user stories were added to the sprint and initially placed in the To Do column. As the work progressed, the stories were moved through the workflow and eventually completed. In Sprint 2, the two selected user stories, “Record Group Expense” and “Assign Expense Shares,” were completed successfully, resulting in all 6 planned story points being completed.

4. What insights did the burndown chart give about your team’s capacity?

The Burndown Chart showed how the remaining story points decreased as the user stories were completed during the sprint. The sprint began with 6 story points and ended with 0 remaining story points. This indicates that the team completed the planned workload within the simulated sprint. The chart also demonstrated how burndown data can be used to compare planned work with actual progress and to understand the team's capacity.
